ID	Task Name	Duration	Start	Finish	Predecessors
1	**Notice To Proceed**	**0 days**	**Thu 5/2/19**	**Thu 5/2/19**	
2					
3	**Concept Definition**	**139 days**	**Thu 5/2/19**	**Wed 11/13/19**	**1**
4	Concept Development	79 days	Thu 5/2/19	Tue 8/20/19	
5	TAC Mtg 1	0 days	Mon 7/15/19	Mon 7/15/19	
6	Public Input Session 1	0 days	Tue 8/20/19	Tue 8/20/19	4
7	Alignment Refinement	38 days	Wed 8/21/19	Fri 10/11/19	6
8	TAC Meeting 2	0 days	Mon 9/9/19	Mon 9/9/19	
9	Public Input Session 2 (TBD)	5 days	Mon 10/14/19	Fri 10/18/19	7
10	Recommended Alignment	15 days	Mon 10/21/19	Fri 11/8/19	9
11	TAC Final Concept Approval	0 days	Wed 11/13/19	Wed 11/13/19	
12					
13	**Preliminary Plans and Cost Opinion**	**60 days**	**Wed 11/13/19**	**Tue 2/4/20**	**11**
14	Preliminary Design	20 days	Wed 11/13/19	Tue 12/10/19	
15	Preliminary Plans	20 days	Wed 12/11/19	Tue 1/7/20	14
16	Quantities and Cost	10 days	Wed 1/8/20	Tue 1/21/20	15
17	TAC Meeting Plan Review	0 days	Tue 1/21/20	Tue 1/21/20	16
18	TAC Preliminary Plan Approval	0 days	Tue 2/4/20	Tue 2/4/20	17FS+10 days
19					
20	**Geotechnical Services**	**90 days**	**Wed 2/5/20**	**Tue 6/9/20**	**18**
21	Global and Foundation Stability	90 days	Wed 2/5/20	Tue 6/9/20	
22					
23	**Easement Documents**	**40 days**	**Wed 2/5/20**	**Tue 3/31/20**	**18**
24	Easements	40 days	Wed 2/5/20	Tue 3/31/20	
25	MODOT Lease Agreement Data	40 days	Wed 2/5/20	Tue 3/31/20	
26					
27	**Permitting**	100 days	Wed 2/5/20	Tue 6/23/20	18
28					
29	**Final Plans, Specifications, Cost Opinion and Construction D**	**80 days**	**Wed 4/1/20**	**Tue 7/21/20**	**23**
30	Final Design	20 days	Wed 4/1/20	Tue 4/28/20	
31	Final Plans, Specifications and CDs	30 days	Wed 4/29/20	Tue 6/9/20	30
32	Quantities and Cost	20 days	Wed 6/10/20	Tue 7/7/20	31
33	TAC Meeting Plan Review	0 days	Tue 7/7/20	Tue 7/7/20	32
34	TAC Documents Approval	0 days	Tue 7/21/20	Tue 7/21/20	33FS+10 days
35					
36	**Approved Documents**	**20 days**	**Wed 7/22/20**	**Tue 8/18/20**	**34**
37					
38	**Start Bidding Services**	**0 days**	**Tue 8/18/20**	**Tue 8/18/20**	36

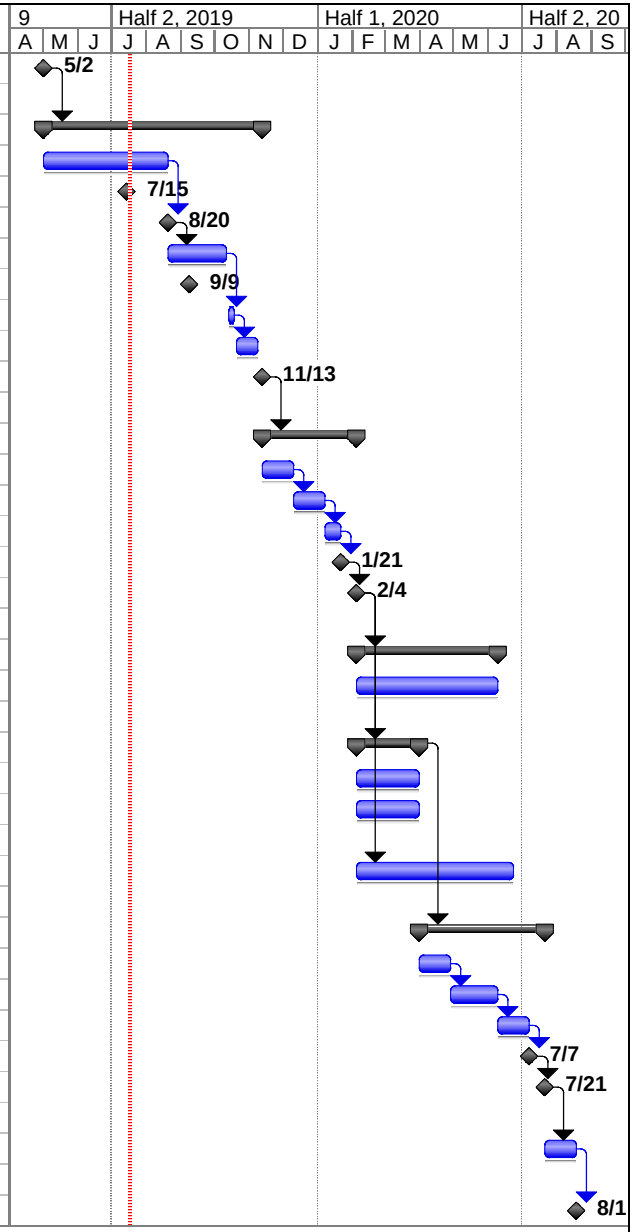

Project: Meramec River Crossing Trail
Date: Wed 7/17/19

Task		Milestone		External Tasks	
Split		Summary		External Milestone	
Progress		Project Summary		Deadline	
